


# THRU-WALL SCUPPER

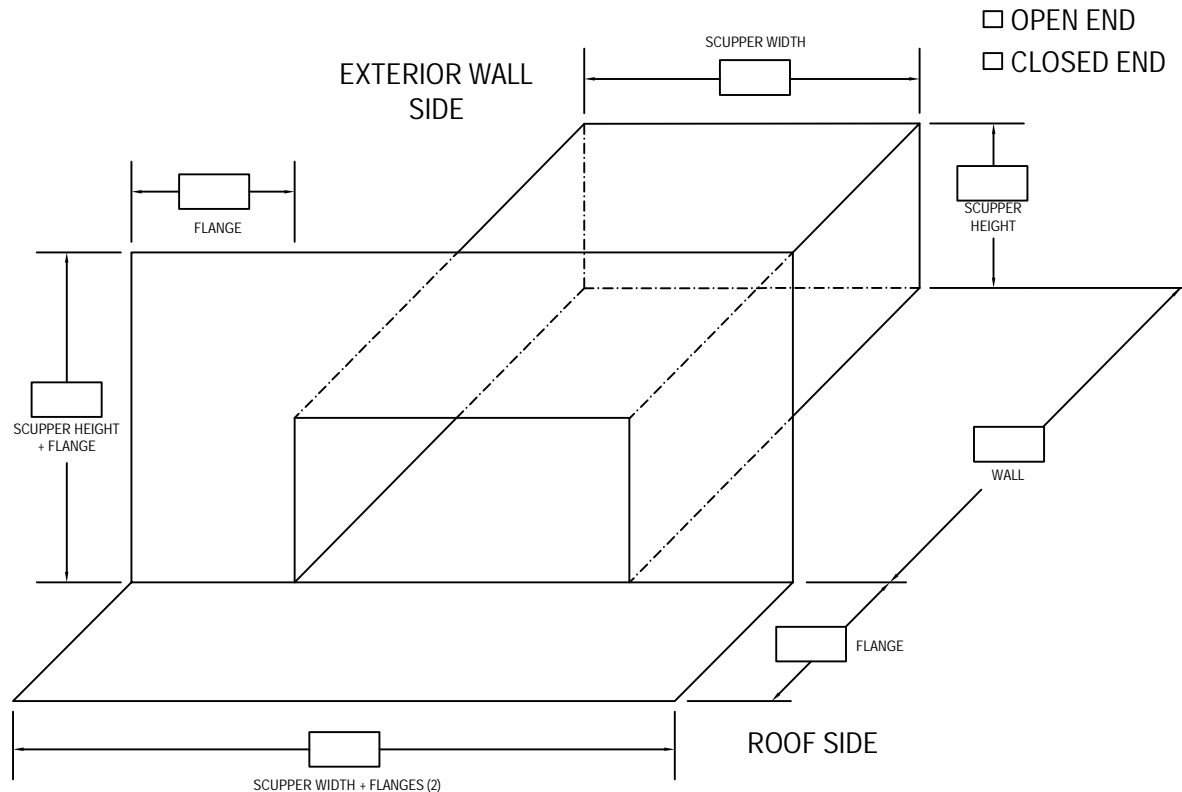

- OPEN END
- CLOSED END

MATERIAL (please choose one):

- |  |  |
|--|--|
| <input type="checkbox"/> 24 GA Steel   | <input type="checkbox"/> .040 Aluminum |
| <input type="checkbox"/> 22 GA Steel   | <input type="checkbox"/> .050 Aluminum |
| <input type="checkbox"/> .032 Aluminum | <input type="checkbox"/> .063 Aluminum |

Other: \_\_\_\_\_

Color: \_\_\_\_\_

Finish: \_\_\_\_\_

Quantities:

\_\_\_\_\_ QUANTITY

\_\_\_\_\_ OUTLET SIZE (IF END IS CLOSED)  
(FIELD INSTALLED)

UNIT Fabrication Requirements:

- |   |   |
|---|---|
| <input type="checkbox"/> Pop Rivet & Sealed | <input type="checkbox"/> Welded (see note)* |
|---|---|

Installation:

- 1) Use roofing manufacturers flange width for roof side to allow proper flashing.
- 2) Welded units recommended.
- 3) Welded units are post painted finish.

Sheet \_\_\_ of \_\_\_ .

DWG# 770-001

**Notes:**

- 1) \*Accessory Welding is only available in 050 aluminum or heavier
- 2) Written approval is required prior to fabrication, contractor is responsible for all dimensions and quantities. Fabricated items are not returnable.

Temple Architectural Products  
1111 Lowell St.  
Elyria, OH 44035

Phone: (440) 323-9393

Fax: (440) 412-7559

Project Name: \_\_\_\_\_

Installing Contractor: \_\_\_\_\_

Contact Name: \_\_\_\_\_

Contact number: \_\_\_\_\_

Signed Approval: \_\_\_\_\_
