


# ALTERNATE DRIP EDGE CLEAT

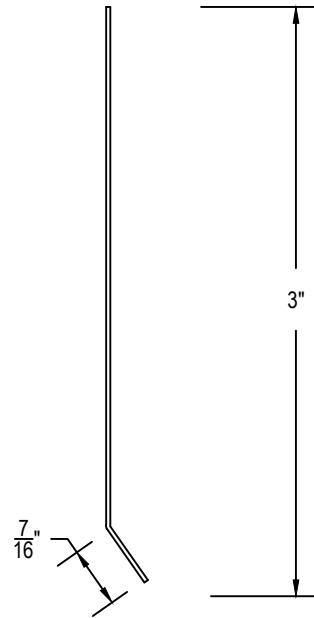

MATERIAL (please choose one):

- 22 GA Steel  
 20 GA Steel

OTHER  
(PARTS ARE MILL FINISH)

OTHER: \_\_\_\_\_

QUANTITIES:

\_\_\_\_\_ Total Linear Feet (10'-0" Lengths)

Miter/End Cap additional information:

See the attached sheets for miters and end cap

Installation:

- 1) Fastened at 6" O/C minimum or otherwise noted.
- 2) 1.5" SS Ring Shank nails, minimum
- 3) Splice plates require 2 beads of sealant per side at splice

Sheet \_\_\_ of \_\_\_.

DWG# 730-009

**Notes:**

- 1) Written approval is required prior to fabrication, contractor is responsible for all dimensions and quantities. Fabricated items are not returnable.
- 2) Parts are mill finish unless otherwise indicated.

Project Name: \_\_\_\_\_

Installing Contractor: \_\_\_\_\_

Contact Name: \_\_\_\_\_

Contact number: \_\_\_\_\_

Signed Approval: \_\_\_\_\_

Temple Architectural Products  
1111 Lowell St.  
Elyria, Ohio 44035

(440) 323-9393  
Estimates@templearchitecturalproducts.com  
www.templearchitecturalproducts.com
